



M | M | P | T

MultiModal Passenger Terminal

NEPA Update

GDOT Intermodal Committee

January 16, 2013



U.S. Department
of Transportation
Federal Transit
Administration



Project and Scoping Overview:

Milestones to Date

- Notice of Intent (April 3, 2012)
- Agency Scoping Meeting (April 17, 2012)
- Public Information Sessions (April 24, May 1, 3)
- Alternatives Development Charrette (July 11, 2012)
- Continued Stakeholder Coordination
- Alternatives Refinement & Evaluation (ongoing since July 11, 2012)
- Agency Meeting December 11, 2012



U.S. Department
of Transportation
Federal Transit
Administration



Georgia Department of Transportation



Project and Scoping Overview:

General Public Scoping Comments

- Timing of project components
- Siting of the project
- Potential treatment of storm water run-off
- Atlanta Constitution Building
- Security consideration for federal buildings
- Impacts during the project's construction



U.S. Department
of Transportation
Federal Transit
Administration



Georgia Department of Transportation



Refinement of Alternatives:

Considerations

- Consolidation of bus transit operations
- Coordination with freight rail operations
- Provide for replacement parking
- Security considerations for federal buildings
- Preservation of historic resources
- Roadway operations



U.S. Department
of Transportation
Federal Transit
Administration




Georgia Department of Transportation



MultiModal Passenger Terminal

Refinement of Alternatives: Common Parcels

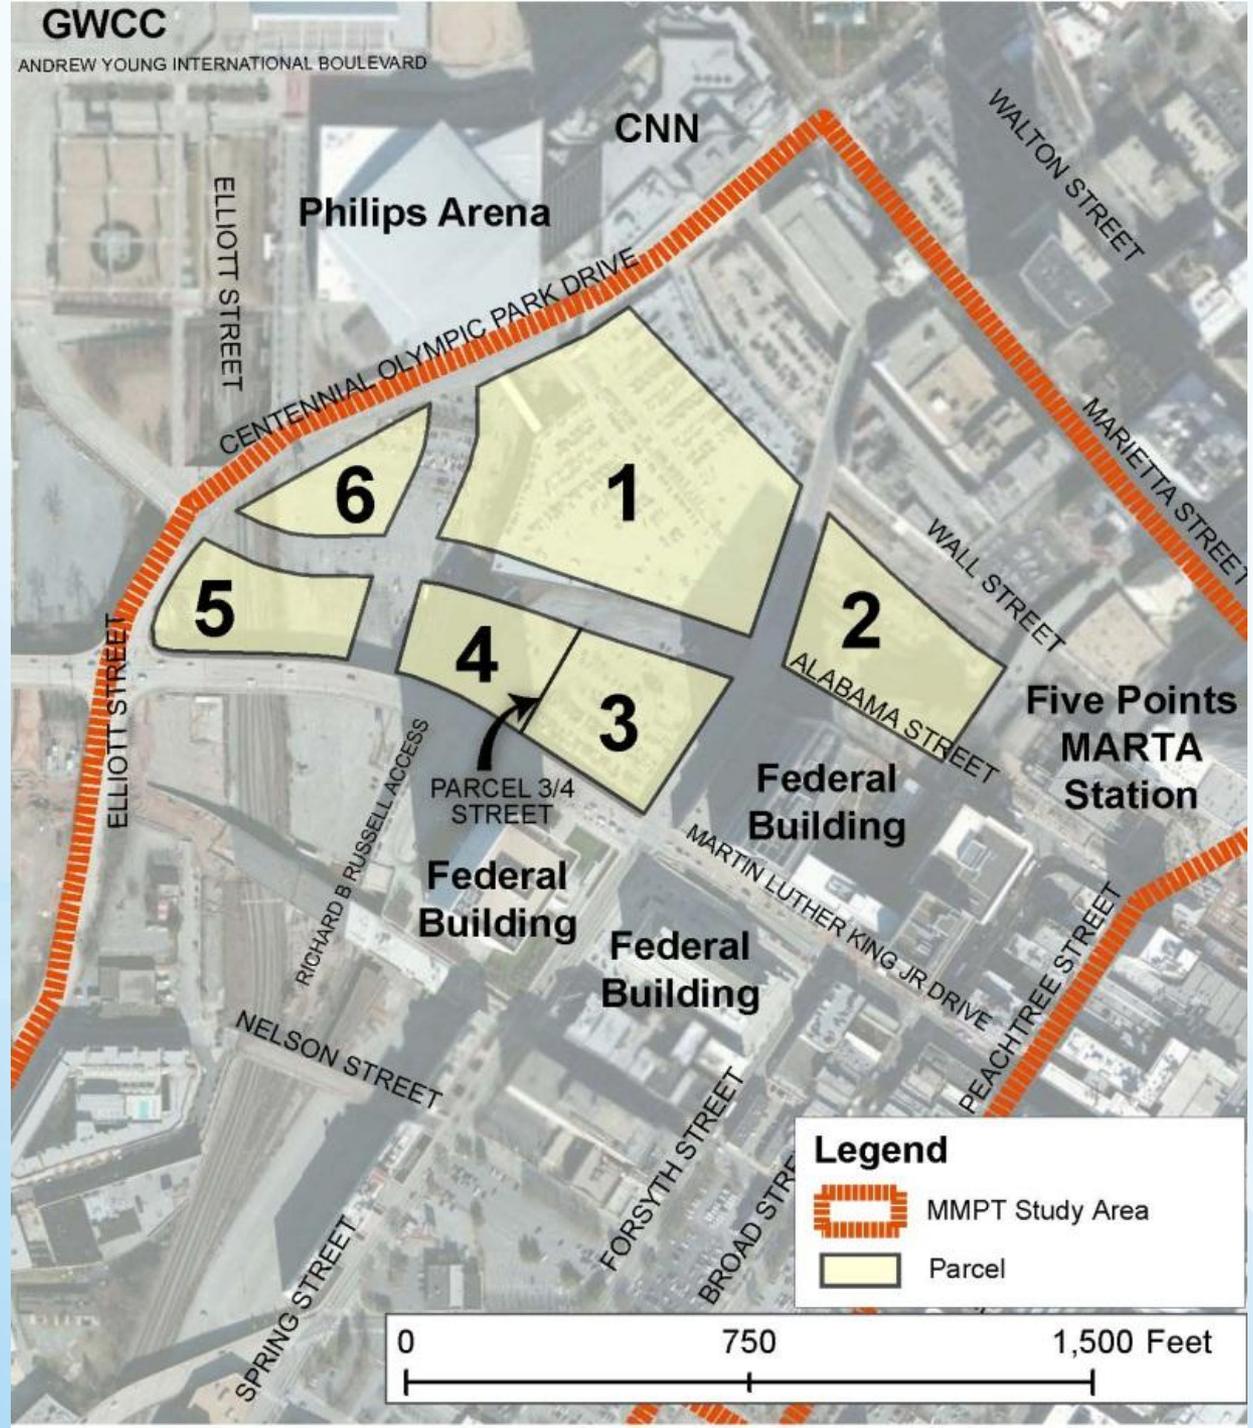

Upcoming Milestones

- Public Information Meeting – Spring 2013
- Agency Review of DEIS – Summer 2013
- Publish DEIS – Fall 2013
- DEIS Public Hearing – Fall 2013
- Publish FEIS – Winter 2013
- Record of Decision – Spring 2014

