

### **Transportation Investment Act (TIA) Update**

Mike Dover, P.E., Georgia Department of Transportation Committee of the Whole-November 20, 2013



### Agenda

- Current Status of Program
- Program Collections and Projections
- Active Projects
- Other Program Activities
- Next Steps and Milestones





## TIA Update-Collections thru September 2013

	Original Revenue Forecast	Actual Revenue Collected	% Behind Forecast
CSRA	\$53,377,295	\$43,681,547	-18%
River Valley	\$38,050,790	\$32,927,583	-13%
Heart of Georgia	\$25,102,139	\$20,361,041	-18%
Total	\$116,530,225	\$96,970,171	-16%





# Disbursements of Revenue Collections

Region	25% Local Governments	75% Approved Investment List
CSRA	\$10,920,387	\$32,761,160
River Valley	\$8,231,895	\$24,695,688
Heart of Georgia	\$5,090,260	\$15,270,780
Totals	\$24,242,542	\$72,727,628





### Active and Completed TIA Construction Projects

# TIA Projects- GDOT Let

111.61100.0010.1100.001111110.600.001	•	Wrightsbor	o Road	l in August	a
---------------------------------------	---	------------	--------	-------------	---

- SR 47 Passing Lanes in Lincoln County
- US 27 widening in Randolph County
- 41 Resurfacing Projects-HOG
- Old Petersburg Road Columbia County
- Eastman Bypass Dodge County

\$19 Million

\$4 Million

\$30 Million

\$1.8 Million

\$34 Million

\$6 Million





### Active and Completed TIA Construction Projects

# TIA Projects-Local Let/NTP for Construction

•	SR 130	Toombs	County-Turn La	ne \$166,000
---	--------	--------	----------------	--------------

- City of Reidsville-2 Resurfacing \$280,000
- Tattnall County Grading and Paving \$467,500
- City of Augusta-4 Resurfacing \$2.2 Million
- City of Vidalia-Adams St Drainage \$1.6 Million
- City of Swainsboro-5 Resurfacing \$660,000
- Telfair County Transit Improvements \$200,000

























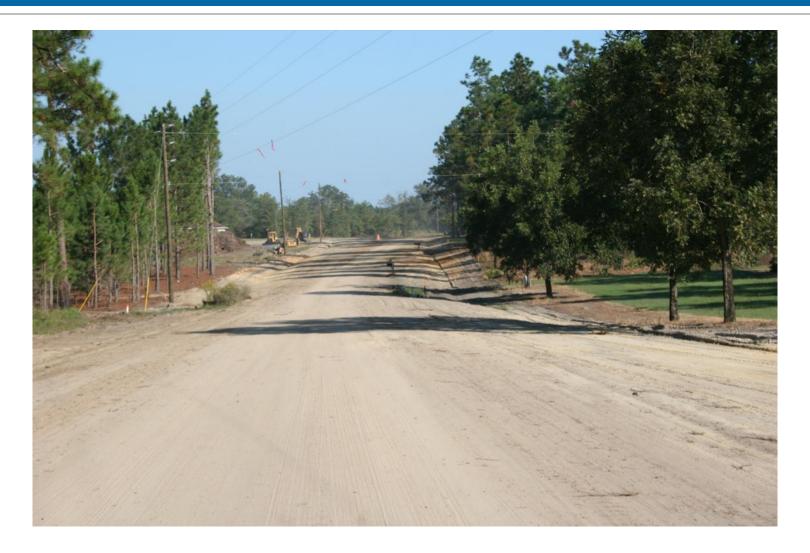





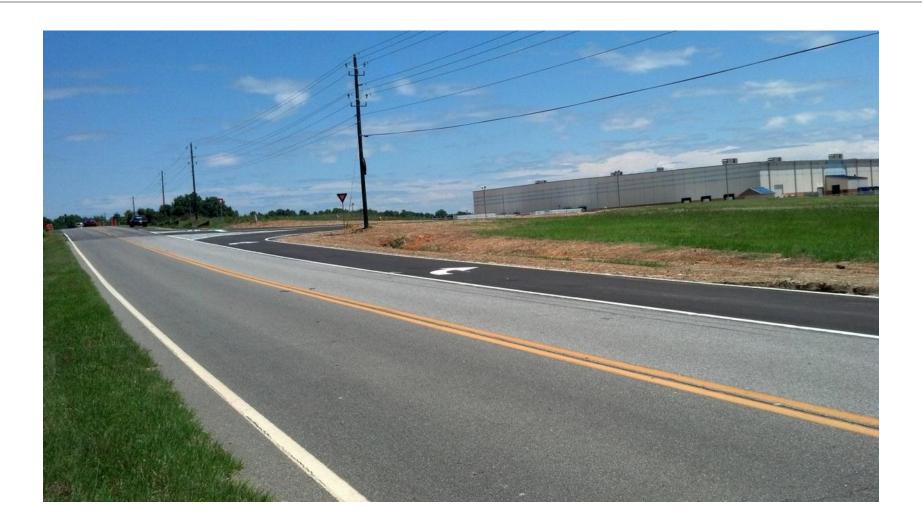





# **Local Discretionary Funds**







# **Local Discretionary Funds**








# **Local Discretionary Funds**







### Band 1 Delivery Responsibilities

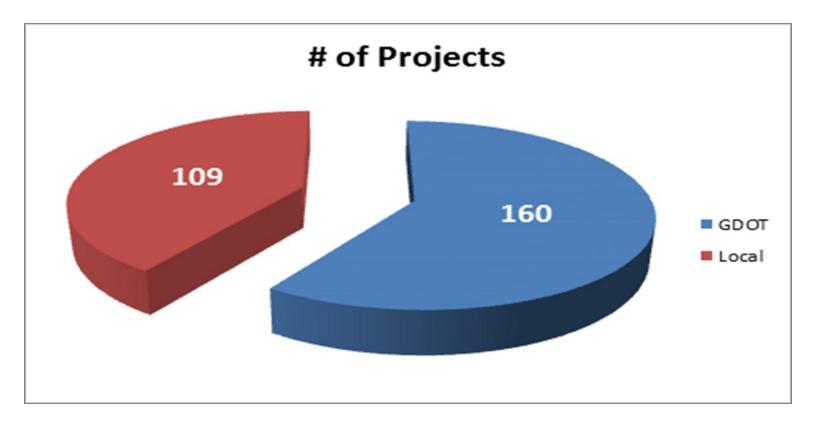


- 269 Total Band 1 Projects
- 47 of 160 GDOT Delivered Projects Let to Construction





### Band 1 PE Project Procurement

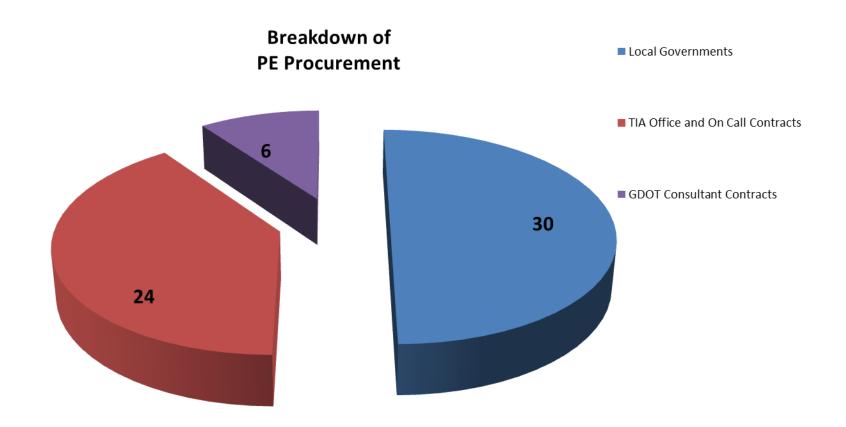





### **Program Activities**

- Continued Coordination with the Citizen's Review Panel for Each Region
  - Program Reporting Due in December
- · Heart of Georgia
  - December 10
- River Valley
  - December 11







- Actively partnering with EEO Office on DBE participation in each of the Regions
- Participant in the DBE Supportive Services
   "Blueprint for Success" Conference
- Provided Project Schedules and Project Types to DBEs within the regions









#### Communications and Outreach



#### Site Navigation


TIA Project Information
TIA Program Fact Sheet
TIA News Room The Institution
Calendar of Public Events The Institution
Meeting Presentations
TIA Manual The Institution
TIA Program Information and Reporting
Project Photograph Gallery
FAQ
Related Links
Contact Us

#### Quick Links





View Projects by Region Below

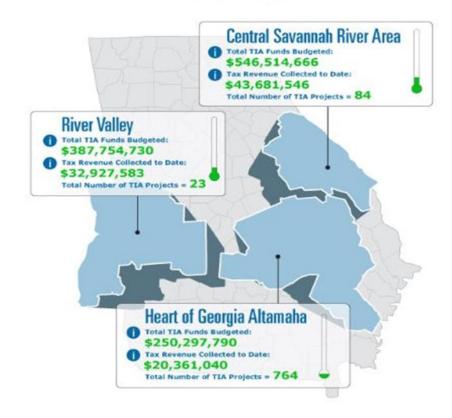





### Communications and Outreach



#### Catch members of the TIA Team out in the community

This week, TIA Staff presents at the 2013 Georgia Transportation Summit November  $7^{\rm in}$ ,

http://business.acecqa.org/events/details/2013-georgiatransportation-summit-16

Last week, staff presented at the ACCG Fall District Meetings across Georgia, and also at the Regional Transportation Summit in Columbus. Visit the TIA calendar of events at <a href="https://www.ga-tia.com/">https://www.ga-tia.com/</a>.

#### News to know

Fall / Winter 2013 - Georgia Transportation Builder, "Meeting the TIA Challenge in Randolph County"

10/8/13 - Georgia Municipal Association, "Projects Begin in Regions with Transportation Sales Tax"

10/8/2013 - State Transportation Board Chair Calls for Statewide Support of TIA

#### Public Hearing Open House-11/7/2013

Information on the New Oconee River Crossing project in Band 1 of the TIA program will be available on Thursday, November 7th from 4-7 PM. The Public Hearing Open House is scheduled at the Laurens County Board of Commissioner's Meeting Room. More info here: <a href="http://www.dot.ga.gov/">http://www.dot.ga.gov/</a> informationcenter/pressroom/PressReleases/Oublin%20Open%20House%20Geacks%20Input%20On%20New%20Oconee%20River%20Bridge%20TIA%20Band%201%20Project%2010-28-2013.pdf



November 4, 2013

The 2012 TIA Manual is currently being revised to include new information and processes. In the interim, new addendums have been posted here: <a href="http://www.qa-tia.com/manuals.aspx">http://www.qa-tia.com/manuals.aspx</a>



Spotted around town. Share your photos at TIA@dot.ga.gov

Questions, comments or to remove your name from our mailing list, please email us at <u>TIA@dot.qa.qov</u>
Visit <u>www.GA-TIA.com</u> for all the latest information on the TIA program.



#### Catch members of the TIA Team out in the community

This work, TIA Administrator Mike Deveris scheduled to update the State Transportation Spend on program activities and programs. Meeting details are available here: http://www.del.co.com/shoutscore/sde/Spend/Desymonis/co.com/shoutscore/sde/Spend/Desymonis/co.com/shoutscore/sde/Spend/Desymonis/

Over the post few weeks, staff met with representatives of Jankins County, Wayne County, Dublin and Augusta to review upon ming TIA projects. Visit the TIA calendar of events at Note: //www.gertin.com/

#### Recently Awarded TIA Projects

Two new projects were just awarded for the TIA program. In Columbia County, 8.4, Snell Contractor was awarded the \$34 million widening of Cild Pateraburg Read including the comativetion of two bridges.

In Dedge County, a \$5 million widening and reconstruction projection 5 R5 7 was a worded to Everett Dykes Grassing Company.

More d'étails are available here: http://www.dot.ga.gov/doing business/contractors/Pages/dofauit.aspx

#### Week of November 19, 2012



Sign of TIA gragress recently spotted in Lincoln County

#### News to Know

See more on the New Geonee River Greating project in Laureina County's cheduled to stort construction in Send 1 of the TIA program from this news atony:

http://www.wgx.a.tv/story/gdoitdissousscarplenartor sonnostinorthilauronaroountur to-dublin 201 31 105

#### Featured Project Photos





Wark by Oxford Construction on USIT/SR1 in Randalph County is underway to meet the targeted completion date of 2016.

 $\xi$  usetions, comments onto remove your name from our mailing list, please email us at TA  $\xi$  dot gaugov. Visit  $g_{NN} \propto 3 - TA$  goog for all the latest information on the TIA grogram.



## **Looking Forward**

- Upcoming projects and lettings
- Monitor collections and forecasts
- Set the pace of the program accordingly
- Develop projects for construction within defined schedule <u>and</u> budget
- Continue to coordinate with local governments





# Questions



