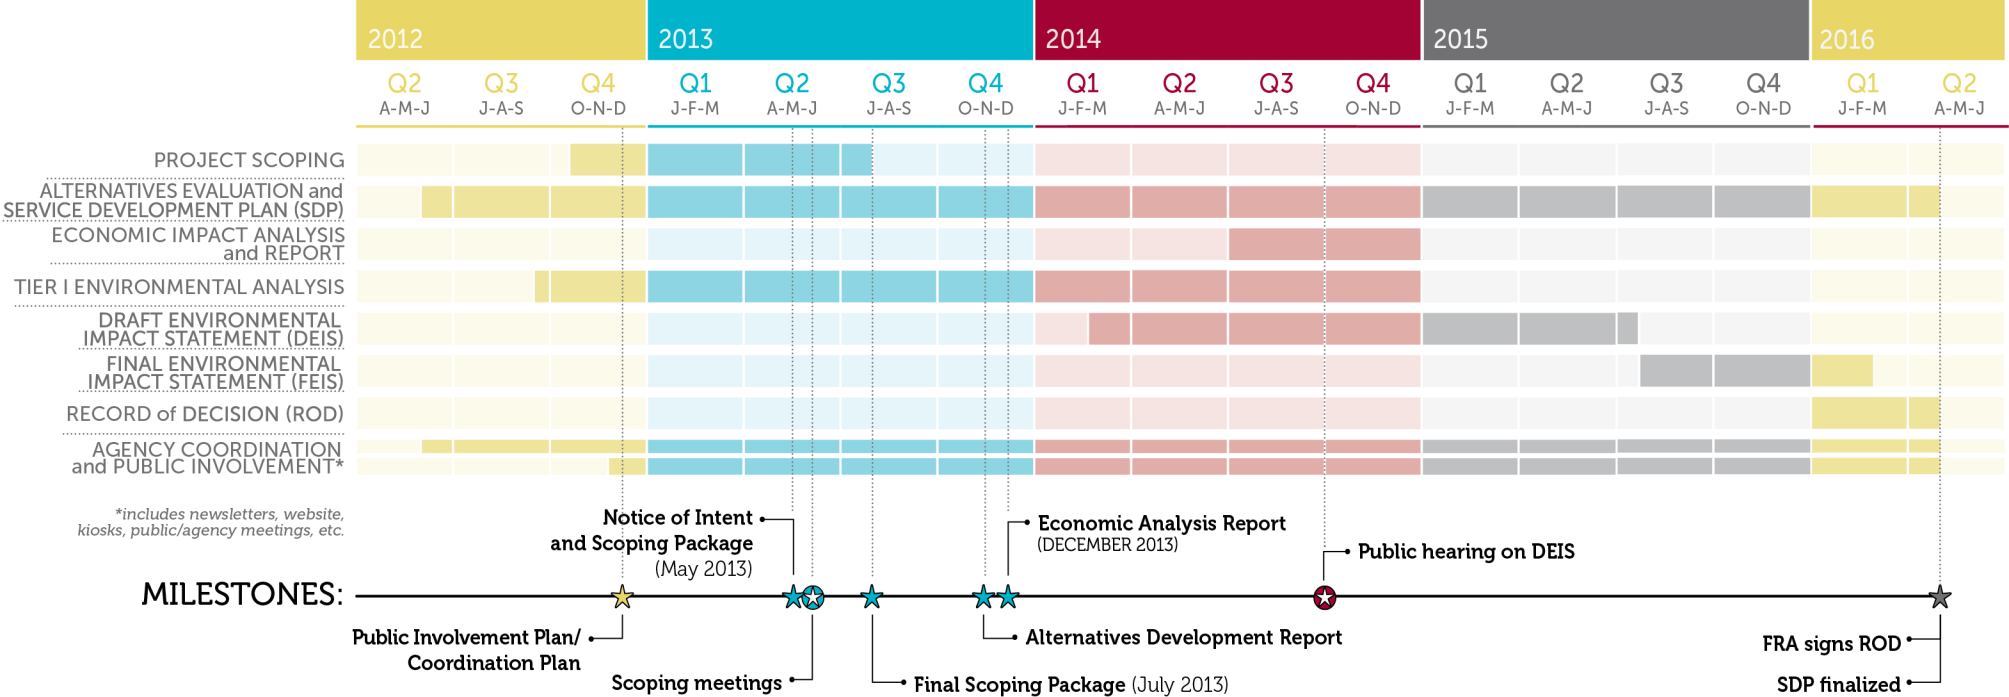
2012
2013
2014
2015
2016
Q2 A-M-J
Q3 J-A-S
Q4 O-N-D
Q1 J-F-M
Q2 A-M-J
Q3 J-A-S
Q4 O-N-D
Q1 J-F-M
Q2 A-M-J
Q3 J-A-S
Q4 O-N-D
Q1 J-F-M
Q2 A-M-J
Q3 J-A-S
Q4 O-N-D
Q1 J-F-M
Q2 A-M-J
PROJECT SCOPING
ALTERNATIVES EVALUATION and SERVICE DEVELOPMENT PLAN (SDP)
ECONOMIC IMPACT ANALYSIS and REPORT
TIER I ENVIRONMENTAL ANALYSIS
DRAFT ENVIRONMENTAL IMPACT STATEMENT (DEIS)
FINAL ENVIRONMENTAL IMPACT STATEMENT (FEIS)
RECORD of DECISION (ROD)
AGENCY COORDINATION and PUBLIC INVOLVEMENT*
*includes newsletters, website, kiosks, public/agency meetings, etc.
MILESTONES:
Notice of Intent and Scoping Package (May 2013)
Economic Analysis Report (DECEMBER 2013)
Public hearing on DEIS
Public Involvement Plan/ Coordination Plan
Scoping meetings
Final Scoping Package (July 2013)
Alternatives Development Report
FRA signs ROD
SDP finalized
